



THREE RIVERS LEVEE IMPROVEMENT AUTHORITY

1114 Yuba Street, Suite 218

Marysville, CA 95901

Office (530) 749-7841 Fax (530) 749-6990

THREE RIVERS LEVEE IMPROVEMENT AUTHORITY

Project Status Report dated August 1, 2008

(Submitted to The Central Valley Flood Protection Board for the August 15, 2008 meeting)

A progress report of the various phases of the Three Rivers Levee Improvement Authority (TRLIA) project is provided in the followings sections of this document. Updates are indicated with italics and underline.

1. Funding Update:

- a. TRLIA plans to prepare a memo to the CVFPB that will describe any proposed changes that are needed in the TRLIA 2nd Implementation Agreement and TRLIA's relationship with the CVFPB. Counsel for the Board is considering this issue.
- b. The TRLIA levee program is fully funded. TRLIA is receiving timely funding from both State and local sources.

2. Levee Design and Construction Work:

a. **Phase 4 – Yuba River Levee between Simpson Lane and the Goldfields:**

- 1) TRLIA has completed the additional hydraulic analysis of the Upper Yuba River and continues to coordinate results with the Corps of Engineers. TRLIA has awarded a design contract to evaluate the south Yuba Levee upstream of Simpson Lane and to design the erosion protection necessary downstream of the Goldfields.

b. **Phase 4 – Feather River Levee between Bear and Yuba Rivers:**

1) **Segment 1 & 3:**

- a) Segment 1: Nordic Inc has completed approximately 45-50% of the levee work and is on target to complete this construction season.
- b) Segment 3: Nordic Inc. is approximately 95% done with levee work and is on target to complete this construction season. TRLIA has received CVFPB staff/Executive Officer approval to construct the seepage berm.

2) **Segment 2:**

- a) TRLIA has awarded major portions of the work defined in Part A of the State encroachment permit. Significant portions of the levee foundation work is underway. Additional levee work is being added to the Teichert contract as landowner access clearances are obtained
- b) The schedule for completion of the Setback Levee is being impacted by the delay in the Corps federal permit approval. Corps HQ has directed that Section 408 approval be obtained before any Section 404 permits are issued for the setback levee construction. The Corps has determined that an EIS is required to support the Section 404 and 408 approvals. The DEIS was published in the federal registrar on July 11. The public comment period ends on August 25. If there are few comments on the DEIS then TRLIA and the Corp of Engineers will strive to have the EIS ROD, 408 approval, and 404 permit be completed by Nov 4; hopefully sooner.
- c) General John McMahon, Corps Division Commander, and Office of Management and Budget staff toured the project area on July 30, 2008. They are supportive of TRLIA efforts to increase flood protection in the RD 784 area.


3. **Building Permits Issued in Plumas Lake Specific Plan Area and North Arboga Study Area in 2007:**

- a. The attached table and graph provides information related to residential building permits issued for the Plumas Lake Plan Area (PLSPA) and the North Arboga Study Area (NASA) within Yuba County in 2008.
- b. As shown in the table, a total of 8 building permits have so far been issued in 2008. No permits were issued in July of 2008.

Attachments:

1. Building permit graphic
2. Building permit table

Building Permits Issued in TRLIA Project Area

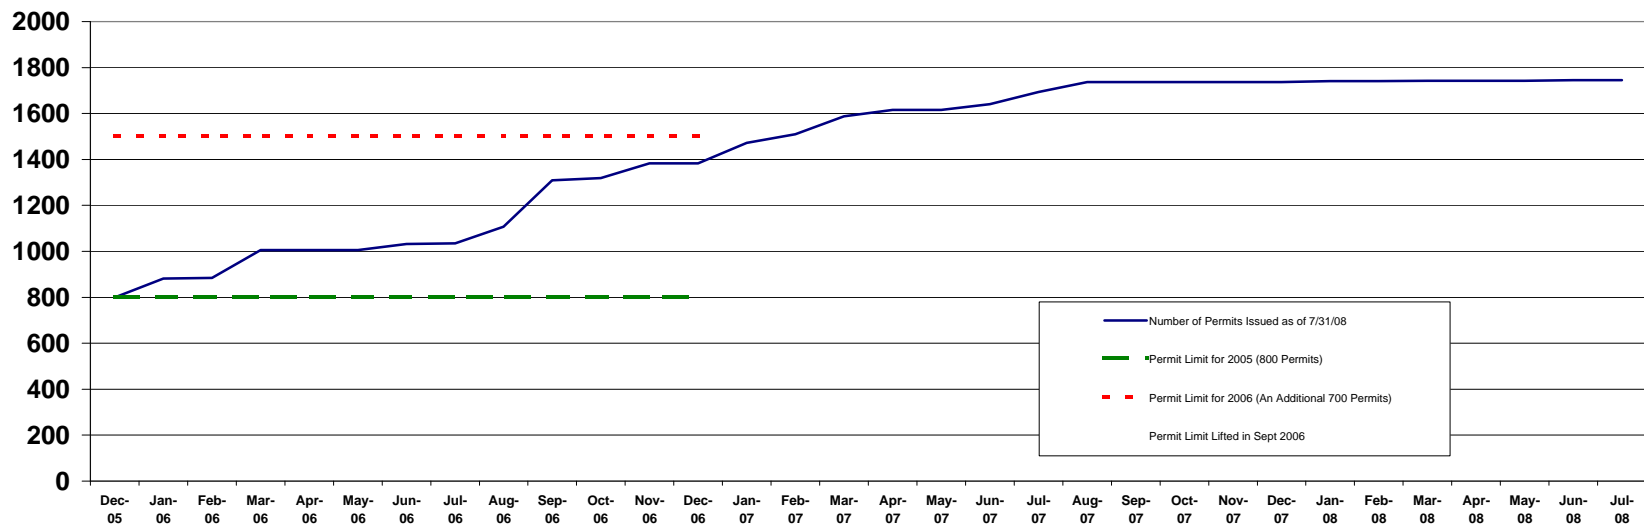

Plumas Lake Specific Plan Area and North Arboga Study Area - Building Permits Issued in 2008

Developer/Builder	Monthly Building Permits Issued for Plumas Lake and North Arboga Study Area														Total (By Builder)
	Jan-08		Feb-08		Mar-08		Apr-08		May-08		Jun-08		Jul-08		
	Plumas	NASA	Plumas	NASA	Plumas	NASA	Plumas	NASA	Plumas	NASA	Plumas	NASA	Plumas	NASA	
KB Homes North Bay															3
Cresleigh Homes															0
Forecast Homes/K Hovnanian	3														3
Homes by Towne/HBT Constr.															0
Beazer Homes															0
California Homes/Home Builders															0
Cassano Kamilos Homes															0
D.R. Horton/Western Pacific															0
Other		1				1									2
Monthly Totals	4		0		1		0		0		3		0		8

As of July 31, 2008

Total Permits for 2008 8
