



# THREE RIVERS LEVEE IMPROVEMENT AUTHORITY

1114 Yuba Street, Suite 218

Marysville, CA 95901

Office (530) 749-7841 Fax (530) 749-6990

## THREE RIVERS LEVEE IMPROVEMENT AUTHORITY

Project Status Report dated October 3, 2008

(Submitted to The Central Valley Flood Protection Board for the October 17, 2008 meeting)

A progress report of the various phases of the Three Rivers Levee Improvement Authority (TRLIA) project is provided in the followings sections of this document. Updates are indicated with italics and underline.

### 1. Administrative Items:

- a. TRLIA plans to prepare a memo to the CVFPB that will describe any proposed changes that are needed in the TRLIA 2<sup>nd</sup> Implementation Agreement and TRLIA's relationship with the CVFPB. Resolution is pending discussions between CVFPB and TRLIA Counsels.

### 2. Levee Design and Construction Work:

#### a. **Phase 4 – Yuba River Levee between Simpson Lane and the Goldfields:**

- 1) TRLIA has begun geotechnical investigations of the Yuba south Levee upstream of Simpson Lane. The purpose of this investigation is to verify the flood protection reliability of this last reach of the Yuba Levee. TRLIA is also beginning the design for erosion protection of the reach just downstream of the Goldfields and expects to construct this erosion protection early next summer.

#### b. **Phase 4 – Feather River Levee between Bear and Yuba Rivers:**

##### 1) **Segment 1 & 3:**

- a) Segment 1: Nordic Inc has completed approximately 85-90% of the levee work and is on target to complete this construction season.
- b) Segment 3: Nordic Inc. is approximately 95% done with levee work and is on target to complete this construction season. The seepage berm for the trench collapse area is nearing completion.

2) **Segment 2:**

- a) All Part A of the State encroachment permit has now been awarded and is under construction. The Fish and Wildlife Service Biological Opinion for the Setback levee has been finalized. The attached site maps show construction progress in various areas.
  
- b) Construction work controlled by Part B of the encroachment permit is still pending waiting for the finalization of the federal permitting process.  
Corps HQ has directed that Section 408 approval be obtained before any Section 404 permits are issued for the setback levee construction. The Corps has determined that an EIS is required to support the Section 404 and 408 approvals. The DEIS was published in the federal registrar on July 11. The public comment period ended on August 25. There were five comment letters. Responses to the comment letters have been prepared and the Administrative Draft of the FEIS has been sent to Corps HQ for review. Schedule is to list the FEIS in the Federal Register on October 24. Once the EIS is completed the issuance of the 404 permit and 408 approval is anticipated to occur shortly thereafter.


3. **Building Permits Issued in Plumas Lake Specific Plan Area and North Arboga Study Area in 2007:**

- a. The attached table and graph provides information related to residential building permits issued for the Plumas Lake Plan Area (PLSPA) and the North Arboga Study Area (NASA) within Yuba County in 2008.
  
- b. As shown in the table, a total of 13 building permits have so far been issued in 2008. Two permits were issued in September of 2008.

Attachments:

1. Building permit graphic
2. Building permit table
3. Progress of Feather Setback Levee Construction (3 Pages)

### Building Permits Issued in TRLIA Project Area

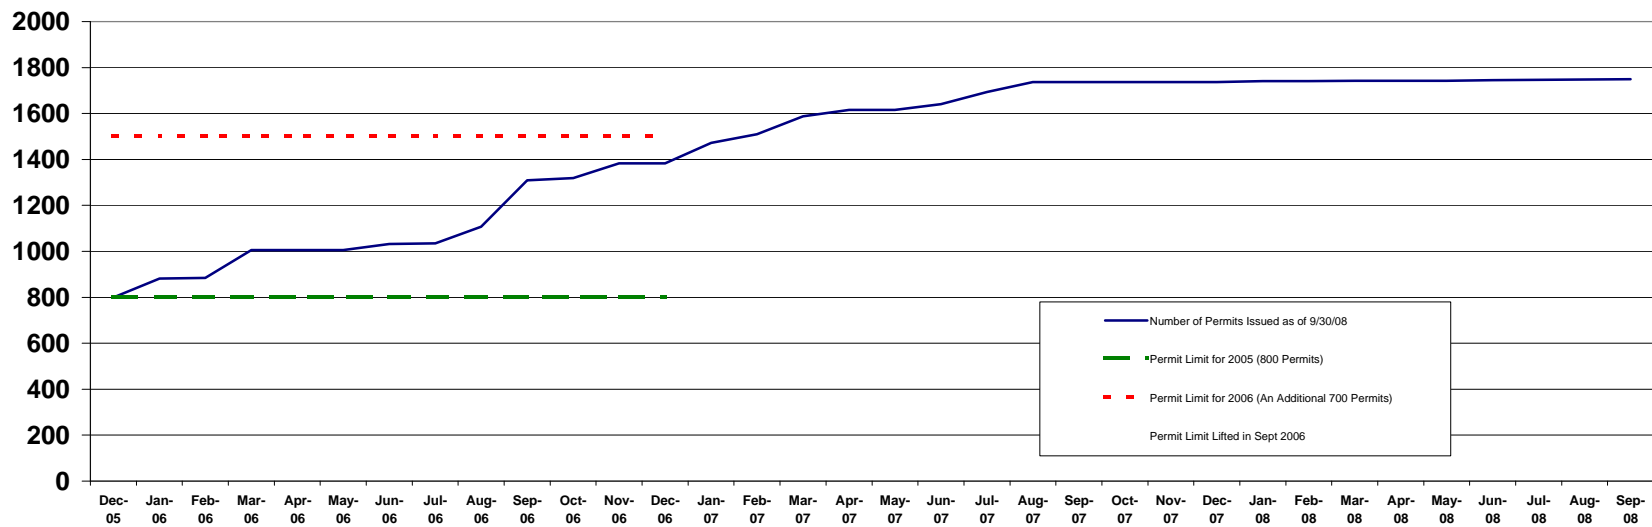

**Plumas Lake Specific Plan Area and North Arboga Study Area - Building Permits Issued in 2008**

Developer/Builder	Monthly Building Permits Issued for Plumas Lake and North Arboga Study Area																Total (By Builder)		
	Jan-08		Feb-08		Mar-08		Apr-08		May-08		Jun-08		Jul-08		Aug-08			Sep-08	
	Plumas	NASA	Plumas	NASA	Plumas	NASA	Plumas	NASA	Plumas	NASA	Plumas	NASA	Plumas	NASA	Plumas	NASA		Plumas	NASA
KB Homes North Bay											3		1					1	7
Cresleigh Homes																	1	1	1
Forecast Homes/K Hovnanian	3																		3
Homes by Towne/HBT Constr.																			0
Beazer Homes																			0
California Homes/Home Builders																			0
Cassano Kamilos Homes																			0
D.R. Horton/Western Pacific																			0
Other		1				1													2
<b>Monthly Totals</b>	<b>4</b>		<b>0</b>		<b>1</b>		<b>0</b>		<b>0</b>		<b>3</b>		<b>1</b>		<b>2</b>		<b>2</b>		<b>13</b>

As of September 30, 2008

**Total Permits for 2008 13**
